South Broward Hospital District
Board Building Committee
Planning and Construction Progress Report
October-24

	_	1		1		October-24			Annuaria		1				0 2 2 2 2	
Project	Status	Contractor	Architect	Budget LTD	Prior Years Expenses	Current FY25	Obligations	Funds Remaining	Approved Contractor Bid Amount	Approved Contingency Amount	On Budget	Contract Type	Board Approval Date	Construction Start Date	Original Construction Completion Date	On Schedule
Joe DiMaggio Children's Hospital - 46																
CT Replacement	Design	TBD	Harvard Jolly Inc.	4,600,000	-	-	79,589	4,520,411	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
JDCH CS MRI Magnet Upgrade	Design	TBD	Harvard Jolly Inc.	1,560,000	-	-	61,527	1,498,473	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Memorial Healthcare System - 10																
MHS IT Data Center ASCO Equipment	Planning	TBD	Gresham Smith	1,000,000	-	-	-	1,000,000	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Primary Care Plantation	Construction	Thornton Construction	Saltz Michelson Architects	1,500,000	151,753	168,203	966,901	213,143	\$924,278	\$ 138,000.00	TBD	Bid	10/27/2023	May 2024	December 2024	Yes
Security Operations Center	Planning	TBD	Gurri Matute	n/a	-	-	-	-	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Employee Health Services Pembroke	Planning	TBD	Saltz Michelson Architects	n/a	-	-	-	-	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
UCC 10175 Pines Blvd	Permitting/Bidding	Lee Construction	Saltz Michelson Architects	4,000,000	123,394	35,582	195,254	3,645,769	. , ,	\$ 227,500.00	Yes	Bid	TBD	TBD	TBD	TBD
MHS Simulation Lab 9581 Premier Parkway	Planning	TBD	TBD	1,200,000	-	-	97,815	1,102,185	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Care Coordination Center	Close Out	Lee Construction	Saltz Michelson Architects	2,623,718	1,162,299	1,018,932	242,135	200,352			TBD	Bid	TBD	September 2023	September 2024	Yes
MHS 7029-7031 Taft Community Youth Services Renovation	Planning	TBD	Gresham Smith	1,443,800	-	-	5,900	1,437,900	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Memorial Hospital Miramar - 45																
Monument Sign Replacements	Permitting/Bidding	Lee Construction	Harvard Jolly Inc.	2,092,000	131,333	210,379	1,531,191	219,098	\$1,728,615	\$ 259,000.00	Yes	Bid	03/27/2024	TBD	TBD	TBD
Memorial Hospital Pembroke - 44																
Red Road Free Standing ED	Permitting/Bidding	DPR Construction	HKS Architects Inc.	17,002,300	1,617,782	105,334	2,084,627	13,194,556	\$22,697,578	\$ 661,095.00	Yes	GMP	10/23/2024	TBD	TBD	TBD
MHP 300 T Chiller/CEP Upgrade	Planning	TBD	Gresham Smith	2,500,000	-	-	9,800	2,490,200	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Free Standing ED	Permitting/Bidding	DPR	HKS Architects Inc.	18,176,100	340,762	574,722	1,759,648	15,500,968	\$37,361,746	\$ 1,088,206.00	Yes	GMP	10/23/2024	TBD	TBD	TBD
MHP MRI Replace with Modular	Planning	TBD	TBD	3,000,000	-	-	-	3,000,000	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Roof Replacement	Permitting/Bidding	TBD	TBD	n/a	-	-	-	-	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
OR Cysto Room	Construction	Lee Construction	Saltz Michelson Architects	2,791,000	247,045	302,395	1,807,380	434,180	\$1,747,842	\$ 262,000.00	Yes	Bid	09/27/2023	09/09/2024	March 2025	Yes
MHP Envelope Repair / Roof Repair	Design	TBD	Other	1,350,000	-	48	4,698	1,345,254	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
	_								_	_			_			
2nd Floor Labor & Delivery MHW CVI #2 Equipment Replacement	Construction Planning	Lee Construction TBD	HKS Architects Inc. TBD	10,779,700 2,526,300	410,734	666,501	3,754,981	5,947,484 2,526,300	\$2,668,050 TBD	\$415,200.00 TBD	Yes TBD	Bid TBD	01/30/2024 TBD	August 2024 TBD	March 2025 TBD	Yes TBD
MHW MCI Shell Space Renovation	Design	TBD	HKS Architects Inc.	2,685,600		-	386,976	2,298,624	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MHW Xray Fluoroscopy Room Equipment Replacement	Design	TBD	Gresham Smith	1,502,400	-	-	52,877	1,449,523	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MCI Conversion to MCVI	Design	TBD	Harvard Jolly Inc.	10,300,000	4,727	82,396	722,604	9,490,273	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MHW MRI Upgrade	Permitting/Bidding	Lee Construction	Harvard Jolly Inc.	2,887,800	, , , , , , , , , , , , , , , , , , ,	77,681	31,322	2,778,797	\$912,030	\$136,804.00	Yes	Bid	TBD	TBD	TBD	TBD
MHW CT Scan Room	Planning	TBD	Gresham Smith	2,186,500	_	-	-	2,186,500	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Envelope Repairs	Permitting/Bidding	TBD	Harvard Jolly Inc.	3,487,700	182,196	16,195	181,395	3,107,914		TBD	TBD	TBD	TBD	TBD	TBD	TBD
										!						
Memorial Manor - 20 Manor Piped-in O2	Hold	TBD	HKS Architects Inc.	352,268		2,350	62,201	287,717	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Manor FEMA Hardening	Permitting/Bidding	TBD	Saltz Michelson Architects	3,250,000	-	82,069	119,582	3,048,349		TBD	TBD	TBD	TBD	TBD	TBD	TBD
Manor Generator/ATS Replacement	Planning	TBD	Saltz Michelson Architects	500,000	-	-	97,747	402,253	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Memorial Physicians Group - 80														•		
MRH MOB Ste 345 OB & MFM	Design	TBD	Saltz Michelson Architects	2,246,500	-	15,600	90,675	2,140,225	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MHM MOB Suite 309 Maternal Fetal Medicine	Design	TBD	Other	1,553,400	-	-	700	1,552,700		TBD	TBD	TBD	TBD	TBD	TBD	TBD
Memorial Primary Care Regional - 640																
Buildout Dania Beach Center	Construction	Lee Construction	Saltz Michelson Architects	3,121,300	69,744	45,959	2,104,239	901,358	\$1,915,242	\$287,000.00	Yes	Bid	03/27/2024	09/16/2024	05/28/2025	Yes
														1		
Memorial Regional Hospital - 40																
Memorial Regional Hospital - 40 MCI Hallandale Expansion	Design	TBD	Harvard Jolly Inc.	4,337,400	-	-	183,945	4,153,455.00	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD

Project	Status	Contractor	Architect	Budget LTD	Prior Years Expenses	Current FY25	Obligations	Funds Remaining	Approved Contractor Bid Amount	Approved Contingency Amount	On Budget	Contract Type	Board Approval Date	Construction Start Date	Original Construction Completion Date	On Schedule
Family Birthplace 4FL	Construction	Turner Construction	HKS Architects Inc.	71,482,200	26,499,521	10,243,608	15,999,154	18,739,916	\$43,850,159	\$4,299,431.00	Yes	GMP	10/26/2022	01/09/2023	April 2025	February 2025
ER Renovation	Construction	Turner Construction	Harvard Jolly Inc.	20,759,500	9,662,710	2,304,995	6,402,138	2,389,657	\$16,401,716	\$1,922,604.00	Yes	GMP	05/25/2022	01/09/2023	August 2025	Yes
Master Plan Surgery & Tower	Design	Robins & Morton	HKS Architects Inc.	37,417,100	9,796,820	2,575,072	3,438,082	21,607,126	TBD	TBD	GMP	TBD	TBD	TBD	TBD	TBD
MRH Bi-Plane Upgrade (Neuro CVI)	Design	TBD	TBD	1,400,000	-	2,000	100,800	1,297,200	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Memorial Regional Hospital South - 41																
HVAC AHU 3	Design	TBD	Saltz Michelson Architects	2,198,400	2,340	1,560	64,896	2,129,604	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MRHS West Tower Remediation	Planning	TBD	TBD	n/a	-	-	-	-			TBD	TBD	TBD	10/21/2024	TBD	TBD
MRHS Pedestrian Bridge Restoration	Design	TBD	KIMLEY HORN AND ASSOCIATES INC	500,000	-	13,500	40,500	446,000	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
Chiller 3 Replacement	Construction	Lee Construction	Saltz Michelson Architects	2,430,000	173,453	132,219	1,465,125	659,203	\$1,456,277	\$218,000.00	Yes	Bid	04/26/2023	12/03/2024	June 2025	Yes
FEMA Wind Retrofit	Construction	Thornton Construction	Saltz Michelson Architects	20,985,000	14,971,859	3,216,349	957,349	1,839,443	\$13,613,113	\$699,802.00	TBD	Bid	TBD	TBD	June 2025	Yes
MRHS CT Imaging Suite Addition	Design	TBD	Harvard Jolly Inc.	1,250,000	-	13,266	66,790	1,169,944	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
IHS Property Management - 83																
MHM 1971 Dr L Davis Blue Water	Construction	Thornton Construction	HKS Architects Inc.	3,800,000.00	101,898.56	1,248,813.24	1,799,368.50	649,919.70	\$2,671,339	\$97,217.00	Yes	Bid	TBD	06/24/2024	December 2024	December 2024
pecialty Pharmacy - 61																
Pharmacy Central Distribution	Design	TBD	HKS Architects Inc.	1,800,000.00	-	-	143,426.00	1,656,574.00	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD

285,663,085.83 65,922,369.67 27,185,130.68 47,420,864.57 145,134,720.91

Amount Awarded \$ 60,059,324.00

\$ 10,887,641.00

\$ 17,208,730.00 \$ 60,251,875.00

DPR

Lee Construction

Thornton Construction
Turner Construction
Robins & Morton



South Broward Hospital District Board Building Committee Construction Progress Report

Construction Services Department

October 2024

Joe DiMaggio Children's Hospital

CT Replacement

Scope of Work: Replace CT & RF equipment and switch existing rooms in order

to minimize equipment down time

Status of Project: Design

Schedule Completion: Anticipated March 2025


Current Status: On Schedule

Architect: Harvard Jolly Inc.

Contractor: TBD

Board Approval Date: Tentative May 2025


Cost of Construction: Estimated \$793,270

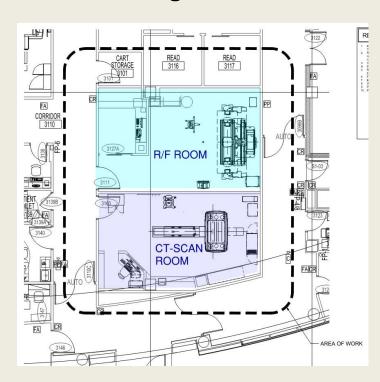

Joe DiMaggio Children's Hospital

Coral Springs MRI Magnet Upgrade

- Scope of Work: Replace MRI components, upgrade room finishes and provide MRI trailer with hook-up connections.
- Status of Project: Design
- Schedule Completion: Anticipated March 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: Tentative April 2025
- Cost of Construction: Estimated \$903,000



MHS IT Data Center ASCO Equipment

- Scope of Work: Replace electrical switchgear serving the data center.
- Status of Project: Planning
- Schedule Completion: December 2025
- Current Status: On Schedule
- Architect: Gresham Architects / TLC Engineering / ASCO
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD





Primary Care Plantation

- Scope of Work: Renovation of approx. 3800 SF of existing offices.
- Status of Project: Construction
- Schedule Completion: December 2024
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: Thornton Construction
- Board Approval Date: October 27, 2023
- Cost of Construction: \$924,278










Security Operations Center

- Scope of Work: Exterior hardening of an existing 6,400 sf building
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gurri Matute
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated TBD


Employee Health Services Pembroke

- Scope of Work: Interior Fit out of existing doctor office, incorporating MHS design standards
- Status of Project: Design
- Schedule Completion: Construction tentative July 2025
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

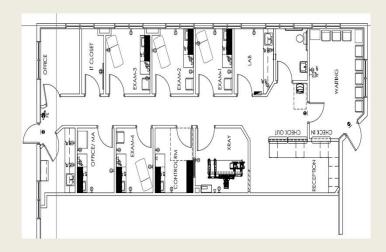

UCC 10175 Pines Blvd.

- Scope of Work: Interior renovation of old Chase bank for a new Urgent Care and Primary Care Center with separate entrances
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: Impacted
- Comments: Pending City approval for plat note amendment
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction
- Board Approval Date: July 24, 2024
- Cost of Construction: \$2,991,000



MHS Simulation Lab 9581 Premier Parkway

- Scope of Work: PHASE 2 Buildout of shell space to include 2-3 classrooms, offices and 1 large sim lab.
- Status of Project: Design
- Schedule Completion: TBD
- Comments: Design ongoing
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1,000,000



Care Coordination Center

- Scope of Work: Centralized Command Center to accommodate 20 employees in approximately 2500 sf at existing Data Building
- Status of Project: Complete. Grand opening October 2024
- Schedule Completion: Completed September 2024
- Current Status: Users moved in October 2024
- Comments: Project completed
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction
- Board Approval Date: January 25, 2023
- Cost of Construction: \$953,046









MHS 7029-7031 Taft Community Youth

- Scope of Work: Replacement of Interior Finishes
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1,790,000



Memorial Hospital Miramar

Monument Sign Replacements

- Scope of Work: Exterior sign replacement 46 signs total
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: LEE Construction
- Board Approval Date: March 27, 2024
- Cost of Construction: \$1,728,615

Red Road Free Standing ED

- Scope of Work: 17,000 SF new construction Free Standing Emergency Department
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: HKS Architects
- Contractor: DPR Construction
- Board Approval Date: October 2024
- Cost of Construction: \$23,358,673



MHP 300 T Chiller/CEP Upgrade

- Scope of Work: Add additional cooling capacity for South Building
- Status of Project: Planning
- Schedule Completion: TBD
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

Douglas Road Free Standing ED

- Scope of Work: 30,000 sq.ft new construction of a Free Standing Emergency
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: HKS Architects
- Contractor: DPR Construction
- Board Approval Date: October 2024
- Cost of Construction: \$38,449,952



MHP Roof Replacement

- Scope of Work: Replace 92,500SF exterior roof
- Status of Project: Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Comments: Bids due 11/11/24
- Architect: Harvard Jolly
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$7M

OR Cysto Room

- Scope of Work: Upgrade equipment and room finishes of Cysto Room #7 and OR #8. 1,035 SF
- Status of Project: Construction
- Schedule Completion: March 2024
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction
- Board Approval Date: October 27, 2023
- Cost of Construction: \$1,747,842



MHP Envelope Repair

- Scope of Work: Paint exterior of MHP, seal cracks, New windows and doors. Approval on MHP ED colors for building - Added scope for shell included in this project.
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

2nd Floor Labor & Delivery

- Scope of Work: Interior Renovation upgrade for existing 14 rooms, (6)
 triage rooms, (1) exam room, nurse's station, and upgraded amenities.
- Status of Project: Construction
- Schedule Completion: March 7, 2025
- Current Status: On Schedule
- Comments: Permit received 11/5/2024
- Architect: HKS Architects
- Contractor: LEE Construction
- Board Approval Date: March 27, 2024
- Cost of Construction: \$2,768,050



MHW CVI #2 Equipment Replacement

- Scope of Work: New Cath Lab Equipment in Room #2 with finish renovations and required changes to MEP
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1.6 Million


MHW MCI Shell Space Reno

- Scope of Work: Tenant improvement design to infill existing 5,160 SQ
 FT shell with infusion bays, exam rooms, offices and restrooms
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: HKS Architects
- Contractor: TBD
- Board Approval Date: Anticipated January 2025
- Cost of Construction: Estimated \$3,354,000




MCI Conversion to MCVI

- Scope of Work: Renovation of existing building to accommodate MCVI functionality including CT and Nuclear CT.
- Status of Project: Bidding and Permitting
- Schedule Completion: December 2025
- Current Status: On Schedule
- Comments: Bids in progress. Bids due 11/11/2024
- Architect: Harvard Jolly
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$4.5 Million

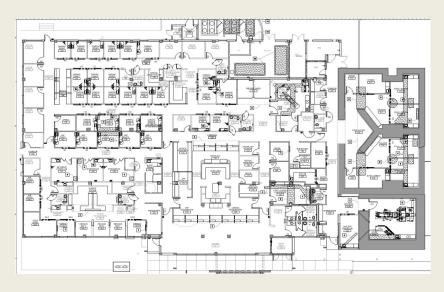

MHW MRI Upgrade

- Scope of Work: Upgrade MRI components and associate equipment, including chiller unit, Liebert unit, electrical panel, etc. To enable the renovations, a temporary MRI Trailer will be set up at the existing adjacent exist previously used for a temporary imagining trailer.
- Status of Project: Permitting
- Schedule Completion: Estimated April 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: Lee Construction Group, Inc.
- Board Approval Date: September 2024
- Cost of Construction: \$912,030

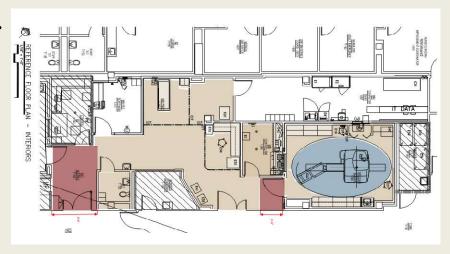

MHW CT Scan Room

- Scope of Work: Move existing CT scan to current ultrasound room and replace CT equipment. Break out project into two packages.
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$1,400,000

Envelope Repairs

Scope of Work: Repair exterior envelope to prevent water intrusion,

replace windows as needed

Status of Project: RFQ process

Schedule Completion: TBD


Current Status: Impacted

Architect: C.B. Goldsmith and Associates, Inc.

Contractor: TBD

Board Approval Date: TBD


Cost of Construction: Estimated \$4,500,000

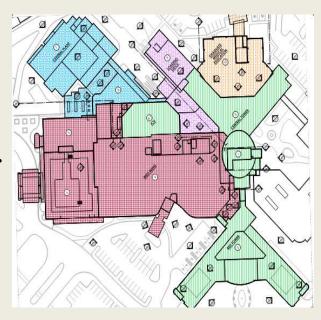

Memorial Manor

Manor FEMA Hardening

- Scope of Work: Exterior hurricane hardening of 1-story nursing home. Work includes reinforcing existing exterior non-reinforced concrete block walls. Reinforcing existing roof trusses, replacing plywood over roof trusses, structural enhancements at gable ends, new metal roof, doors, windows and louvers.
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Comments: Bid documents are in process
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$7,400,140

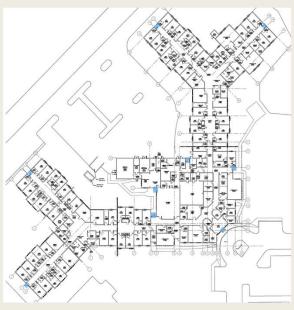

Memorial Manor


Manor Generator/ATS Replacement

- Scope of Work: Replacement of generator and automatic transfer switch
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$500,000

Memorial Physicians Group

MRH MOB Suite 345 OB & MFM

- Scope of Work: 5300 SF renovation combining two specialties (High Risk OB and Maternal Fetal Medicine).
- Status of Project: Design
- Schedule Completion: January 2026
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: April 2025
- Cost of Construction: \$1.525 M

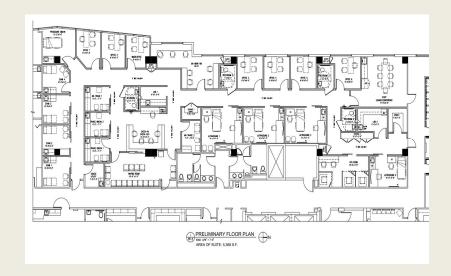

Memorial Physicians Group

MHM MOB Suite 309 Maternal Fetal Medicine

- Scope of Work: Renovation of existing 2,675 SF
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

Memorial Primary Care

Buildout Dania Beach Center

- Scope of Work: Build out of shell space 4680 sf to include: 15 exam rooms; 5 Providers (3 PCP and 2 Specialty); 5 PFSRs (at check in/check out); 6 Mas; 1 Office Practice manager
- Status of Project: Construction
- Schedule Completion: June 2024
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction
- Board Approval Date: March 27, 2024
- Cost of Construction: \$1,915,242






MCI Hallandale Expansion

- Scope of Work: Expand existing MCI Hallandale clinic to add 22 infusion bays,
 7 exam rooms, 5 blood draw stations and support spaces
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD



MRH Therapy Room #1 Linac Replacement

- Scope of Work: Replacement of the existing MRH Linear Accelerator equipment in Therapy Room #1, finishes and cabinetry
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

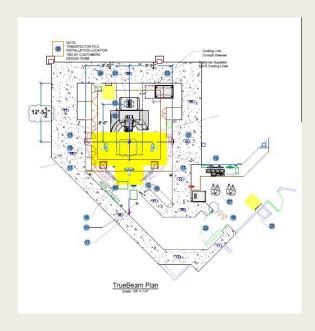

Family Birthplace 4th Floor

- Scope of Work: Full renovation of 65,000sf for MRH 4th Floor Family Birthplace (56 mother/baby beds and 18 antepartum/obstetric observation unit)
- Status of Project: Construction
- Schedule Completion: February 2025
- Current Status: On Schedule
- Architect: HKS Architects
- Contractor: Turner Construction
- Board Approval Date: October 26, 2022
- Cost of Construction: \$43,850,159









ER Renovation

- Scope of Work: MRH ED Interior Finishes. Full interior finish renovation including flooring, wall covering, doors, ceiling, restrooms with plumbing fixtures, nursing station replacement, casework, etc. (35,049 SF). 1,200 sf of new construction to accommodate decontamination showers and exam room, expanded storage, and improved EMS lounge. Additionally, the project involves 4,500 sf of renovations to improve the layout, efficiency and patient access within the existing 3 trauma bays and resuscitation room. 5700 SF
- Status of Project: Construction
- Schedule Completion: May 2025
- Current Status: On Schedule
- Comments: Phase 1 of Trauma expansion complete January 2025
- Architect: Harvard Jolly
- Contractor: Turner Construction
- Board Approval Date: May 25, 2022
- Cost of Construction: \$16,401,716









Memorial Regional Hospital

Master Plan Surgery and Tower

- Scope of Work: Build new 8 story patient and surgical tower with 3 story connector. Scope includes interior renovation of several areas on the 1st and 2nd floors (Main lobby, Registration, Heart Clinic, OR Suite, SPD, Material Management, etc.) Upgrade existing MEP infrastructure to support new spaces
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Comments: Moving into permitting and bidding phase November 2024
- Architect: HKS Architects
- Contractor: Robins & Morton
- Board Approval Date: Expected March 2025
- Cost of Construction: TBD






Memorial Regional Hospital

MRH Bi-Plane Upgrade

- Scope of Work: Equipment replacement of Neuro Bi Plane Hybrid OR
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD

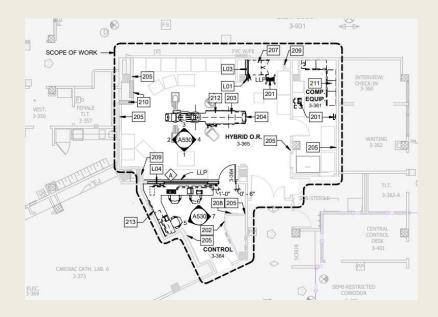

Memorial Regional Hospital

MRH Chiller Replacement

- Scope of Work: Chiller replacement planned by MRH including electrical and plumbing upgrades.
- Status of Project: Planning
- Schedule Completion: TBD
- Engineer: Davila Engineering
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD





HVAC AHU 3

- Scope of Work: Replacement of AHU-3
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$1,200,000

MRHS West Tower Remediation


- Scope of Work: Remediation of the West tower facade to mitigate moist air entering the building
- Status of Project: Planning
- Schedule Completion: TBD
- Comments: Working with envelope consultant on Design
- Architect: HKS Architects
- Contractor: Thornton Construction
- Board Approval Date: TBD
- Cost of Construction: TBD






MRHS Pedestrian Bridge Restoration

- Scope of Work: Pedestrian bridge structural restoration.
- Status of Project: Bidding/ Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Kimley-Horn & Associates
- Contractor: TBD
- Board Approval Date: January 2025
- Cost of Construction: Estimated \$1,200,000

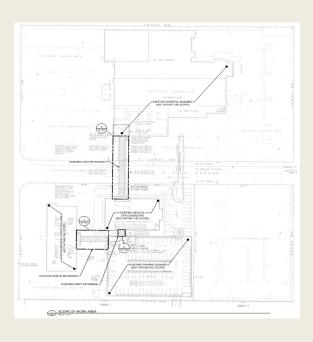

Chiller 3 Replacement

- Scope of Work: Replace Chiller #3 and associated cooling tower with new equipment in the same location
- Status of Project: Construction
- Schedule Completion: June 5, 2025
- Current Status: On Schedule
- Comments: Chiller to arrive mid- Nov.
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction
- Board Approval Date: April 26, 2023
- Cost of Construction: \$1,456,277

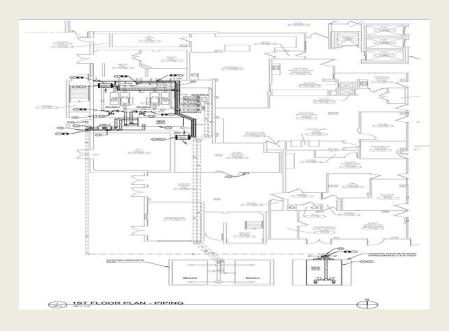

FEMA Wind Retrofit

- Scope of Work: FEMA granted MRHS \$7.1 million to utilize for the hardening of our building. During this project, we will be hardening the East Tower.
 Additionally, the project includes interior remediation of the east tower extending the original interior to the new exterior façade.
- Status of Project: Construction
- Schedule Completion: January 2025
- Architect: Saltz Michelson Architects
- Contractor: Thornton Construction
- Board Approval Date: June 23, 2021
- Cost of Construction: \$16,521,557









MRHS CT Imaging Suite Addition

- Scope of Work: The project consists of converting existing Ultrasound space for a new CT Scan Room and control room. The scope requires reconfiguration of the existing Nuclear medicine for 3 new Ultrasound rooms. Additionally, merging imaging and surgery waiting area and creating a chapel on third floor.
- Status of Project: Design
- Schedule Completion: Design to be completed by 02/14/25
- Current Status: On Schedule
- Architect: Harvard Jolly
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1.1M





MHS Property Management

MHM 1971 Dr Davis Blue Water

- Scope of Work: Interior fit out of 7260 SQ FT. The scope includes new exam rooms, procedure rooms, offices and workstations. New doors, ceiling and flooring.
- Status of Project: Construction
- Schedule Completion: 12/20/24
- Current Status: On Schedule
- Architect: HKS Architects
- Contractor: Thornton Construction
- Board Approval Date: May 25, 2022
- Cost of Construction: \$2,671,339








Specialty Pharmacy

Pharmacy Central Distribution

- Scope of Work: Create a central pharmacy distribution center with limited budget approved for FY25
- Status of Project: Design
- Schedule Completion: Anticipated December 2024
- Current Status: On Schedule
- Architect: HKS Architects Inc.
- Contractor: TBD
- Board Approval Date: February 2025
- Cost of Construction: Estimate \$1,300,000

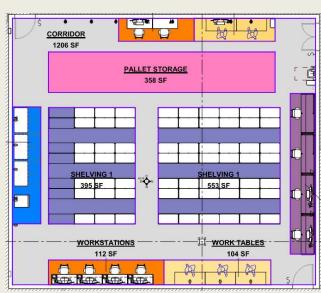



MEMORIAL REGIONAL HOSPITAL · MEMORIAL REGIONAL HOSPITAL SOUTH · JOE DIMAGGIO ♥ CHILDREN'S HOSPITAL MEMORIAL HOSPITAL WEST · MEMORIAL HOSPITAL MIRAMAR · MEMORIAL HOSPITAL PEMBROKE · MEMORIAL MANOR

TO: Shane Strum

Interim Chief Executive Officer

FROM: Mark Greenspan

Vice President

Construction and Property Management

SUBJECT: Bid Opening: MCI Conversion to MCVI at Memorial Hospital West

DATE: November 11, 2024

Bids for the MCI Conversion to MCVI at Memorial Hospital West were opened at 4:30 P.M. on Monday, November 11, 2024, in the Executive Conference Room. In attendance were Commissioner Brad Friedman, Leah Carpenter, David Smith, Joseph Kadis, Joseph Stuczynski, Carmen Gonzalez, and Mark Greenspan. Attending via telephone were Babette Kosar, Patrick Connor, Teddy Speropoulos, and Felicia Turnley, and representatives from Engel Construction, Inc., Lee Construction, Inc., Lego Construction Co., and Thornton Construction Company, Inc.

The following bids were received for the MCI Conversion to MCVI at Memorial Hospital West:

	Engel Construction, Inc.	\$ 5,920,395.60
\triangleright	Lee Construction Group, Inc.	\$ 5,699,505.00
\triangleright	Lego Construction Co.	\$ 7,570,505.25
\triangleright	Thornton Construction Company, Inc.	\$ 5,725,496.00

Mr. Greenspan informed the group, as has been the standard practice, that the bids would be reviewed and verified for accuracy.

Recommendation for award will be presented at the next regularly scheduled Board Building Committee Meeting.



MEMORIAL REGIONAL HOSPITAL · MEMORIAL REGIONAL HOSPITAL SOUTH · JOE DIMAGGIO ♥ CHILDREN'S HOSPITAL MEMORIAL HOSPITAL WEST · MEMORIAL HOSPITAL MIRAMAR · MEMORIAL HOSPITAL PEMBROKE · MEMORIAL MANOR

TO: Shane Strum

Interim Chief Executive Officer

FROM: Mark Greenspan

Vice President

Construction and Property Management

SUBJECT: Bid Opening: Roof Replacement at Memorial Hospital Pembroke

DATE: November 11, 2024

Bids for the Roof Replacement at Memorial Hospital Pembroke were opened at 4:30 P.M. on Monday, November 11, 2024, in the Executive Conference Room. In attendance were Commissioner Brad Friedman, Leah Carpenter, David Smith, Joseph Kadis, Joseph Stuczynski, Carmen Gonzalez, and Mark Greenspan. Attending via telephone were Babette Kosar, Patrick Connor, Teddy Speropoulos, and Felicia Turnley, along with representatives from Engel Construction, Inc., Lee Construction, Inc., Lego Construction Co., and Thornton Construction Company, Inc.

The following bids were received for the Roof Replacement at Memorial Hospital Pembroke:

\triangleright	Engel Construction, Inc.	\$ 7,994,911.20
\triangleright	Lee Construction Group, Inc.	\$ 4,981,200.00
\triangleright	Lego Construction Co.	\$ 3,840,661.65
	Thornton Construction Company, Inc.	\$ 4,645,940.00

Mr. Greenspan informed the group, as has been the standard practice, that the bids would be reviewed and verified for accuracy.

Recommendation for award will be presented at the next regularly scheduled Board Building Committee Meeting.
